Exclusive Headless Website

Proposal for Lakeshore Hospital and Research Centre Ltd

April 14, 2026

Prepared for

E: info@lakeshorehospital.com | **P:** +91-484-2701032

A: VPS Lakeshore, NH-66 Bypass, Maradu, Nettoor P.O, Kochi - 682040, Kerala.

Table of Contents

Table of Contents **1**
Cover Letter **3**
Revision History 4
1. Document Preface and Scope of Work **5**
1.1 Preface 5
1.2 Scope of Work 5
1.2.1 Business Analysis and Wireframing 5
1.2.2 UI/UX Designing 5
1.2.3 UI/UX Development using Next JS 6
1.2.4 Backend Development using Strapi 6
1.2.5 Basic Onsite SEO, Optimization, and Proofreading 6
1.2.6 Quality Assurance 8
1.3 Out of Scope 9
2. Specification and Deliverables **9**
2.1 Website Specifications 9
2.2 Deliverables 10
3. Service Fee* **11**
3.1 Website Design and Development 11
3.2 Budget Breakdown 11
3.3 Payment Terms 12
3.4 Optional Services 13
4. Post-Development Support **14**
5. Execution Team **15**
5.1 Work Coordination 15
5.2 Resource Structure 16
5.3 Anticipated Execution Timeline 17
6. Services & Tech **18**
7. Our Services and Commitments **18**
8. Change Control Procedure **19**
8.1 Project Change Control Procedure 19
8.2 Request for Change Form 20
8.3 Terms of Agreement 21
8.4 Consent for the Release 22
9. Escalation Procedure **23**
10. Closure Note Acceptance Procedure **23**
11. Terms and Conditions **25**
11.1 Permissions and Copyright 25
11.2 Termination Terms 25

Copyright © Webandcrafts 2026. All Rights Reserved.

12. Why us? 26
13. Next Step 27
14. Approval from the Client 28
Appendix I - Recent Works from Healthcare Domain 29
Appendix II - Case Studies 31
Appendix III - Client References 32
Appendix IV - Recommended Server Configuration 33
Appendix V - Recommended AI Addons 34

This document contains confidential information and is intended for the sole use of Lakeshore Hospital and Research Centre Ltd and represents Webandcrafts' intellectual property. This document represents a proposal of services or a contract between Webandcrafts and the concerned team.

Cover Letter

Dear Sir / Ma'am

Thank you for considering Webandcrafts for this association. We feel privileged to be associated with Lakeshore Hospital and Research Centre Ltd for this project.

With the experience gained over the years in website development, I feel assured to commit to designing and developing an exclusive headless website for Lakeshore Hospital.

This document outlines the scope of work and pricing of our services. If you have any questions, please contact us directly over email or phone.

To accept this proposal, please sign below.

Thank you!

Anoop K Joseph
Global Sales Head
Webandcrafts.

anoop@webandcrafts.com
+91-8606 48 33 99

Copyright © Webandcrafts 2026. All Rights Reserved.

Revision History

Version	Date	Remarks
1.0	26-12-2025	Proposal drafted based on the discussion with Mr. Anil.
2.0	01-04-2026	Scope revised based on the discussion with the Lakeshore team and price updated accordingly.
3.0	14-04-2026	Modifications made based on the discussion with Mr. Chandran and Mr. Paul.

spec-lakeshore-bepsoke-web-v3.0 | Copyright © Webandcrafts 2026. All Rights Reserved.

1. Document Preface and Scope of Work

1.1 Preface

The agreement between "**Webandcrafts**"- referred to as "we/us" across the document, is pleased to submit this proposal for website development for "**Lakeshore Hospital and Research Centre Ltd**", referred to as "Company/you/your" across the document. We recognize the significance of the project and the positive impact the new website to be built would have on your business. We also appreciate the level of effort you have expended in the past interacting with us to share information about the goals and objectives of this project, current business processes, and supporting systems which is a good first step for beginning the Digital Transformation Journey. This project aims at

1. Developing a customized solution that delivers your desired functionality
2. Incorporate the functionality without impairing website performance or aesthetics
3. Offer the assistance you need to customize and grow

1.2 Scope of Work

Our scope of service includes the following:

1.2.1 Business Analysis and Wireframing

Our team of business analysts and product consultants will study your business strategy, processes, and portfolio to determine which proven and emerging technologies will work best to boost productivity and revenue, meet evolving customer requirements, and ensure the security of your data.

1.2.2 UI/UX Designing

A qualified UX analyst from our team would define a layout after taking into consideration the most efficient and market-proven strategies that can optimize the overall output of the system. Our team of UI designers would then work on it to convert them into aesthetically precise user interfaces.

Copyright © Webandcrafts 2026. All Rights Reserved.

1.2.3 UI/UX Development using Next JS

Converting the site design into search engine friendly and standards compliant HTML / CSS, as well as any JavaScript required for animations, hover effects, drop-downs, etc. Next.js is a minimalistic framework for server-rendered React applications as well as statically exported React apps. It gives the best user experience with all the features : hybrid static & server rendering, TypeScript support, smart bundling, route prefetching, and more.

1.2.4 Backend Development using Strapi

We will configure the Strapi Backend to suit the comprehensive requirement of this application. The setup backend would be integrated with the developed layout, mandating all the necessary procedures required.

1.2.5 Basic Onsite SEO, Optimization, and Proofreading

Our content writing team will be proofreading all site content, and our SEO team will be performing basic SEO optimization. Content writing would be out of our scope of service. We anticipate receiving them all on your behalf.

- ➔ **Research and Analysis**
  - **Website analysis and reporting**
    The website will be analyzed thoroughly to identify all possible performance issues, and a detailed report will be prepared by the SEO analyst.
  - **Keyword research**
    A list of relevant keywords is formulated further to a thorough market analysis process. The keywords will be carefully sorted and finalized, aiming for efficient search result ranking.
  - **Initial keyword rank check**
    Analysis of the current ranking of the website, in terms of popular and targeted keywords. The report thus furnished would help plan further strategies.
  - **Backlink analysis**
    Analyze and implement backlinking to other websites and search results in order to make the website more identifiable within popular searches.

Copyright © Webandcrafts 2026. All Rights Reserved.

➔ **On-Page Optimization**

- **Title tag optimization**
  The HTML titles defined on the website are optimized to come up more frequently in the search results.
- **Meta tags optimization**
  With the assistance of the SEO analyst, the developer implements efficient meta tags in the code.
- **URL optimization**
  Website URLs are optimized using targeted keywords and other strategies, to make them more identifiable by popular searches.
- **Heading tags optimization**
  Implementing header tags in the HTML codes, based on the SEO and keyword analysis report.
- **Content optimization**
  All the website content is carefully structured, by a content writing specialist, who is well-versed in developing keyword-specific and SEO-aiding content.
- **Plagiarism checking**
  The developed content is cross-verified to ensure that the content is not plagiarized.
- **Image optimization**
  Product images or other images used on the website are optimized to enhance the site load speed.
- **Internal link optimization**
  Links within the web pages are redirected within the domain after carefully planning out. The aim is to improve Google indexing of all the pages within the website.

spec-lakeshore-bepsoke-web-v3.0 | Copyright © Webandcrafts 2026. All Rights Reserved.

- **HTML validation checking**
  The developed HTML code is validated for syntax errors like open tags, extra spaces, forgotten quotation marks, etc. The check is done using third-party tools and helps improve the page speed ranking.
- **Speed and performance testing**
  The website speed and performance under varied load conditions are analyzed.
- **Robots.txt optimization**
  Using the robot exclusion protocol/standard the search engine is instructed on which pages to crawl from the website.
- **Duplicate URL optimization**
  All possible URLs that might pose an issue of URL duplication is identified and optimized. This if left unchecked can affect the search ranking of the website.
- **Sitemap creation**
  The website site map is appropriately linked so that the search engine easily identifies all the pages on the website.

1.2.6 Quality Assurance

The system once developed, and while still being hosted on our local servers would be subjected to stringent quality assurance processes. The various stages involved would be as listed below:

1. **Cross Browser testing** - Ensuring consistency across all major browsers and platforms.
2. **Cross-Platform testing** - The system will be checked for consistency on different platforms, inclusive of macOS, Windows, iOS, Android, etc.
3. **Device Testing** - We prefer testing the website on real and handheld devices to ensure that there are no missing links during the QA. Our team is equipped with all the major Android and iOS devices to conduct the process.

spec-lakeshore-bepsoke-web-v3.0 | Copyright © Webandcrafts 2026. All Rights Reserved.

1.3 Out of Scope

1. **Contents to be published across the website**
   All textual (product descriptions, business, marketing and site material) would be out of our scope of service. We anticipate to receive them all on your behalf.
2. **Photographs and videos**
   All company related Image and video submission would be under the purview of your responsibility. We anticipate receiving them all on your behalf.
3. **Third party APIs and Plugin License Purchases**
4. **Domain and Hosting**
5. **Progressive SEO and Digital Marketing**

2. Specification and Deliverables

2.1 Website Specifications

1. Feature List : Link
2. Exclusive layouts for web pages
3. Headless Architecture
4. Front End Development using Next JS
5. Backend Development using Strapi
6. Role based permission system on the backend
7. RTL and LTL support (English and Arabic)
8. Third-Party Integrations
9. Compliant with DPDPA and HIPAA standards
10. Manual and System Testing
11. Adaptiveness/Support range

Copyright © Webandcrafts 2026. All Rights Reserved.

- Responsiveness across devices (website in Desktops, Laptops, and Mobile browsers)
    - Safari (13.0 and above)
    - Chrome (104.0 and above)
    - Edge (100.0 and above)
    - And other major browser's stable versions

2.2 Deliverables

1. **Website Source files for Deployment**
   The ownership of the website source files would be transferred back to the client once the final payment is remitted.
2. **Deployment in the preferred host**
3. **Knowledge Transfer (KT) sessions for the Content Management System (On/Offsite)**
   We will set up detailed knowledge transfer sessions remotely at a preferred date and time suggested by the client.
4. **Onsite SEO** on the deployed website (live domain)

spec-lakeshore-bepsoke-web-v3.0 | Copyright © Webandcrafts 2026. All Rights Reserved.

3. Service Fee*

∗The price mentioned in this section was quoted from the mentioned requirements;
∗Webandcrafts will take the privilege to change in the future if requirements are bound to change;
∗GST will be additional if paid from a domestic account

3.1 Website Design and Development

We propose to **Design and Develop**

An Exclusive Headless Website for **Lakeshore Hospital**

using Strapi and Next js

at an agreed rate of **₹22,00,000**

3.2 Budget Breakdown

Sl. No	Task	Man Hours
1	Business Analyst	40
2	Project Manager	80
3	UI/UX Designer	350
4	Frontend Developer	850
5	Backend Developer	550
6	Tester	80
Total		**1950**

Specification	Total (INR)
Exclusive Headless Website	₹26,65,000
Discount	₹4,65,500
Total	**₹22,00,000**

Copyright © Webandcrafts 2026. All Rights Reserved.

3.3 Payment Terms

1. **Payment Split**
    a. 50% of the total quoted amount in advance on confirmation of our quotation.
    b. The second milestone (25%) is defined at the completion of UI design.
    c. The final installment (remaining 25%) of the payment should be remitted after project completion before going live.
2. The payment should be made within 7 days from the date of issuance of the invoice.
3. For any delay in payment after the due date, 12% of the total amount payable will be charged.
4. Payment once remitted shall not be returned.
5. Webandcrafts holds the right to hold the development in case of delay in payment.
6. The proposed quote has a validity of 15 days, from the date of its preparation.
7. Failure of Payment: In case of failure or delay in payment as per the raised invoice. The work shall be put on hold temporarily until further intimation from you.

Bank Account Details:

Federal Bank

Account Name: webandcrafts

Account Number: 16505500000658

Bank Name: Federal Bank

Branch: Koratty Infopark

IFSC: FDRL0001650

SWIFT Code: FDRLINBBIBD

spec-lakeshore-bepsoke-web-v3.0 | Copyright © Webandcrafts 2026. All Rights Reserved.

3.4 Optional Services

Service	Specification	Tenure	Amount (INR)*
PCI Certified security auditing	One time auditing. If required on a regular basis, may have to sign up with auditors	One-time	₹ 1,00,000
	Developer fixes	One-time	₹ 25,000
Server	As referred above in Section 1.2 above; Cloud will be billed based on the usage every month by the provider directly	Monthly	Price depends on server specs
	Monitoring and Support for Cloud	Monthly	Starts from ₹15,000
	CDN and WAF	Monthly	₹2,500
Website Maintenance	Maintenance (25 man-hours). Any developments beyond allocated hours will be billed in an hourly based resource allocation. Billing rates mentioned in section 4 will be applicable for such tasks.	Monthly	₹30,000
Copywriting	Copywriting in English and Arabic	One-time	₹5 per word
Progressive SEO	10-15 Keywords and 2 blogs per month	Monthly	₹75,000
Digital Marketing	10 Creatives	Monthly	₹75,000

**GST will be additional if paid in iNR*

Copyright © Webandcrafts 2026. All Rights Reserved.

4. Post-Development Support

If a bug is identified on the system at any time within 30 days after launch, it will be fixed without any charge.

Any developments beyond the scope module could be sorted in hourly-based resource allocation at the billing rate mentioned below.

Resources	Hourly Billing Rate (INR)
UI/UX Designer	₹1500
Business Analyst/ Project Manager	₹1250
Next JS Developer	₹1350
Strapi Developer	₹1350
QA Tester	₹1250

spec-lakeshore-bepsoke-web-v3.0 | Copyright © Webandcrafts 2026. All Rights Reserved.

5. Execution Team

5.1 Work Coordination

Team	Member	Designation	Experience
Account Manager	Anoop K J	Global Sales Head	10+ yrs
Project Manager	Subin	Sr. Project Manager	8+ yrs
	Jisam	Project Manager	4+ yrs
Business Analyst	Sanjay	Sr. Business Analyst	6+ yrs
	John	Business Analyst	4+ yrs
Solution Architect	Vinoth Kumar	CTO	13+ yrs
	Sharath L K	Solution Architect	10+ yrs
UI/UX Designer	Clint Antony	Chief Designing Officer	12+ yrs
	Nidheesh	Sr. UX Designer	7+ yrs
	2 other UI/UX Designers		2 - 5 yrs
Frontend Developer	Mohammed Latheef	UI Developer Lead	9+ yrs
	4 other Frontend Developers		2 - 5 yrs
Backend Developer	Akash	CMS Lead	8+ yrs
	2 other Strapi Developers		2 - 5 yrs
QA	Manu	QA Lead	6+ yrs
	2 other QA Analysts		2 - 5 yrs
SEO	Sreeved	Digital Marketing Lead	8+ yrs
	1 other SEO Analyst		2 - 5 yrs

Copyright © Webandcrafts 2026. All Rights Reserved.

5.2 Resource Structure

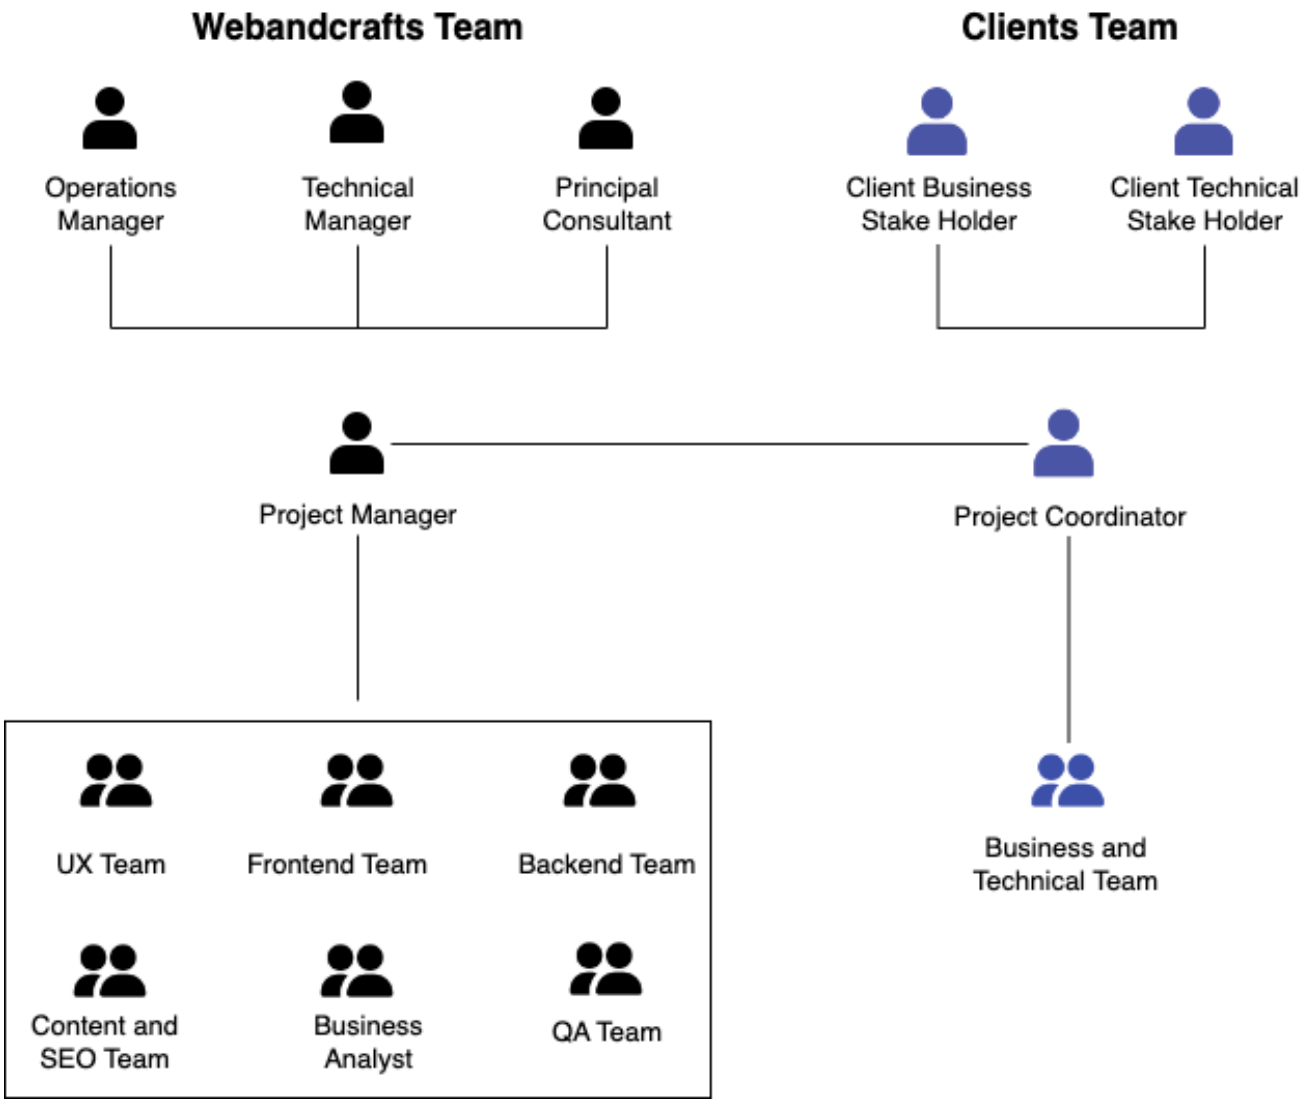

Copyright © Webandcrafts 2026. All Rights Reserved.

5.3 Anticipated Execution Timeline

Disclaimer: The dates in the table above are estimates based on our experience with similar website development projects. While we strive to accurately estimate project timelines in every proposal, we reserve the right to move delivery dates in response to unforeseen delays or changes to project requirements.

Stage	Completion (Working Days)
Project Kickoff Meeting	Day 01
Complete UX Screens	Day 25
Complete Strapi Development	Day 40
Complete UI Development	Day 70
Complete API Development	Day 72
Complete API Integration	Day 80
Testing & Bug Fixes	Day 88
Website Launch	Day 90

spec-lakeshore-bepsoke-web-v3.0 | Copyright © Webandcrafts 2026. All Rights Reserved.

6. Services & Tech

1. We will assign a Project Manager to oversee the project and serve as a single point for engagement communication. We will also assign Business Analysts, Designers, Frontend Developers, Backend Developers, or other IT specialists as the requirement demands.
2. The developers will be working on the approved designs and the functionality discussed to achieve engagement goals.
3. Before final deployment, the application will be subjected to stringent quality assurance procedures to ensure a fault-free product.
4. The completed system will be made available on the live domain further to the client's approval.

7. Our Services and Commitments

- ➔ Project management, communications, and tracking will be primarily handled by email, over the phone (and/or Skype), and through the Online Chat system available on our official website.
- ➔ Unless an existing website analytics account is provided, site analytics, goal tracking, and analytics will be handled by Google Analytics.

Events that may delay final delivery or individual milestone delivery include

- ➔ delays in receiving your approvals.
- ➔ delays in receiving the 3rd party application API Credentials or any dependable account.
- ➔ delays in receiving your feedback & revision notes.
- ➔ delays in receiving partial payments to initiate project or individual completed phases.

spec-lakeshore-bepsoke-web-v3.0 | Copyright © Webandcrafts 2026. All Rights Reserved.

8. Change Control Procedure

8.1 Project Change Control Procedure

A Project Change Request (PCR) would be the channel for communicating the change. The PCR document must describe the change, the rationale for the change, and the impact the change would have on the project.

- ➔ The designated Project Manager of the requesting party would review the proposed change and determine whether to submit the request to the other party.

- ➔ Once submitted, both the Project Managers would review the proposed change and agree to implement it or recommend it for further assessment or reject it.

- ➔ In the event, the proposed change necessitates further assessment and "Webandcrafts" requires additional effort and cost for such assessment, "Webandcrafts" would specify such charges to "Company". Further, "Company " Authorized representative would authorize "Webandcrafts" to raise an invoice to "Company" for such charges as per the terms of this SoW and the Agreement.

- ➔ The outcome of the assessment would determine the impact that the implementation of the PCR would have on price, schedule, and other terms and conditions of this SoW and the Agreement.

- ➔ A PCR must be signed by authorized representatives from both parties to authorize the implementation of any agreed changes to the SoW and the Agreement. Until a change is agreed in writing, both parties would continue to act in accordance with the latest agreed and signed version of the SoW.

- ➔ A PCR that has been signed by authorized representatives from both parties constitutes a change authorization for purposes of this SoW and the Agreement.

spec-lakeshore-bepsoke-web-v3.0 | Copyright © Webandcrafts 2026. All Rights Reserved.

8.2 Request for Change Form

Request for Change		
Change Authorization to the Agreement between "Company Name" and "Webandcrafts" dated ("Agreement").		
Name of the System:		
Change Authorization #:	RFC/	Date:
Originator of Request:	"Webandcrafts"	
RFC Project Start/ End Date:	DD-MM-YYYY	DD-MM-YYYY
Type of Change (Check one) ☐ *Functional* ☐ *Performance* ☐ *Editorial*		
Reason for Change:		
Description of Change: 1. The differential Price of the revised Bill of Quantity is .....Taxes: Included/ Excluded 2. RFC contains Existing Items () or New Items () 3. RFC value is Inclusive () or Exclusive of Taxes 4. Separate PO would be released for the RFC: Yes () or No () 5. Except to the extent varied by this Change Authorization, all the terms of the Agreement referred shall continue to remain in full force and effect.		
Commercial impact of the change: Payable By _____ (Tick below as applicable) ☐ *One Time,* _____ *Only.* ☐ *Recurring,* _____ *Only Per Month/ Quarter, Starting Date* _____		
Authorized Signatory "Company Name" Name: Designation: Date:	**Authorized Signatory** "Webandcrafts" Name: Designation: Date:	

Copyright © Webandcrafts 2026. All Rights Reserved.

8.3 Terms of Agreement

1. **Authorization** - "Company" is engaging "Webandcrafts", as an independent contractor for the "Company" website development, deployment, hosting, & support.

2. **Payment** - Fees to "Webandcrafts" are due in accordance with the above-listed pricing table. Fees for monthly services will be invoices on the 1st business day of each calendar month and are due on a net-30 basis.
3. **Completion** - "Webandcrafts", and "Company" must work together to complete the project in a timely manner. "Webandcrafts" agrees to work expeditiously to complete the project no later than the launch date (depending on the date of acceptance of the agreement).
4. **Assignment of Project** - "Webandcrafts" reserves the right to assign subcontractors to this project to ensure the right fit for the job as well as on-time completion.
5. **Revision During Execution -** "Company" may be charged additional fees if it decides to make changes to the agreed-upon project scope and objectives.
6. **Legal & License** - "Webandcrafts" warrants that the functionality contained in this project will meet "Company" requirements and that the operation will be reasonably error-free.

   The entire risk as to the quality and performance of the project is with the "Company". In no event will "Webandcrafts" be liable to "Company" or any third party for any damages, including any lost profits, lost savings, or other incidental, consequential or special damages arising out of the operation of or inability to operate the website, even if "Webandcrafts" has been advised of the possibility of such damages.

   If any provision of this agreement shall be unlawful, void, or for any reason unenforceable, then that provision shall be deemed severable from this agreement and shall not affect the validity and enforceability of any remaining provisions.
7. **Copyrights & Trademarks** - "Company" represents "Webandcrafts" and unconditionally guarantees that any elements furnished to "Webandcrafts" for inclusion in the project are owned by "Company", or that "Company" has permission from the rightful owner to use each of these elements, and will hold

Copyright © Webandcrafts 2026. All Rights Reserved.

harmless, protect, and defend "Webandcrafts" and its subcontractors from any claim or suit arising from the use of such elements furnished by "Company".

8. **Copyright to Project** - "Webandcrafts" guarantees that all aspects of the design and construction of the project will be disclosed to "Company" upon completion, and full code, copyrights, and ownership will be the sole property of "Company". "Webandcrafts" retains the right to display graphics and other design elements as examples of its work in its portfolio.
9. **Sole Agreement** - The agreement contained in this Contract constitutes the sole agreement between "Webandcrafts" and "Company" regarding this project. Any additional work not specified in this contract must be authorized by a written change order. All prices specified in this contract will be honored for three (3) months after both parties sign this contract. Continued services after that time will require a new agreement.
10. **Initial Payment & Refund Policy -** If "Company" halts work and applies for a refund within 4 days, work completed shall be billed at the hourly rate of the hourly rate, and deducted from the initial payment, the balance of which shall be returned to "Company". If, at the time of the request for a refund, work has been completed beyond the amount covered by the initial payment, "Company" shall be liable to pay for all work completed at the hourly rate stated above.
11. **COVID-19 Clause** - The parties acknowledge and agree that COVID-19 is an event beyond the parties' reasonable control, and it is not possible to foresee (or advisable to try and foresee) its duration, impact, or extent (including measures and recommendations that may be put in place by regulators). As such, where a party's non-monetary obligations are not performed, affected, and/or delayed and that is attributable to COVID-19 or its related impacts, notwithstanding any other provision in the agreement, the affected party will not be responsible for such non-performance, affected performance or delay. The parties will act reasonably to discuss the affected obligations, potential workarounds, and related issues in good faith and will document any agreed changes to the agreement.

8.4 Consent for the Release

Any version of the project shall be released for public access only after explicit consent of your team, conveyed through email.

Copyright © Webandcrafts 2026. All Rights Reserved.

9. Escalation Procedure

The following procedure would be followed if the resolution is required to a conflict arising during the performance of this Statement of Work. When a conflict arises between **"Company"** and **"Webandcrafts"**, the project team member(s) would first strive to work out the problem internally.

- ➔ **Level-1**: If the project team cannot resolve the conflict within two (2) business days, the **"Company"** Project Manager and **"Webandcrafts"** Project Manager will meet to resolve the issue.
- ➔ **Level-2**: If the conflict is not resolved within three (3) business days after being escalated to Level-1, the **"Company"** Project Executive would meet with the **"Webandcrafts"** Chief Operating Officer or Chief Technology Officer to resolve the issue.
- ➔ **Level-3**: If the conflict is not resolved within three (3) business days after being escalated to Level-2, the **"Company"** Executive would meet with the **"Webandcrafts"** Chief Executive Officer to resolve the issue.
- ➔ During any conflict resolution, **"Webandcrafts"** agrees to provide Services relating to items not in dispute, to the extent practicable pending resolution of the conflict. **"Company"** agrees to pay invoices per this SoW and the Agreement.

10. Closure Note Acceptance Procedure

The purpose of a 'Closure Note' is to assess the project, ensure completion, and derive any lessons learned and best practices to be applied to future projects. Confirming the project has met all sponsor, customer, and stakeholder requirements. Verifying that all deliverables have been delivered and accepted, would be reviewed and accepted in accordance with the following procedure:

- One (1) printed copy or an email soft copy of the Deliverable Material would be submitted to the "Company" Project Manager, seeking a sign-off with the mail subject as "Project Closure Note". It will be your Project Manager's responsibility to make and distribute additional copies to any other reviewers.

Copyright © Webandcrafts 2026. All Rights Reserved.

- Within five (5) business days, which time frame shall not impact the project progress; the “Company” Project Manager would either accept the Deliverable Material or provide “Webandcrafts” Project Manager a written list of identified defects in regard to the agreed specification. If there is no response from your Project Manager received within the above-mentioned period, then the Deliverable Material and the “Project Closure Note” will be ‘deemed accepted’.
- In case “Company” provides feedback within five (5) business days of the original submission, “Webandcrafts” would resubmit the updated version within five (5) business days to your Project Manager for review and final acceptance sign-off. If no response from your Project Manager is received within the above period, then the Deliverable Material and the “Project Closure Note” will be ‘deemed accepted’.
- In case of a dispute on deemed acceptance, then the number of days of delay beyond five (5) business days would be added to the target dates for all subsequent milestones and the project plan would be amended accordingly. The impact of such delay in sign-off and the consequent impact of delay in the project plan would be addressed through the Project Change Control procedure. Additionally, the “Company” should not levy any penalty for the delay.
- “Webandcrafts” would request in writing from “Company” reasons or shortfalls of the system, if any, if the system is put into production use without acceptance. Such a response from “Company” would be provided within twenty (20) business days of “Webandcrafts” request. However, if no response is received from “Company” within twenty (20) business days without assigning any reasons or shortcomings to “Webandcrafts” then the system would be deemed accepted.

spec-lakeshore-bepsoke-web-v3.0 | Copyright © Webandcrafts 2026. All Rights Reserved.

11. Terms and Conditions

11.1 Permissions and Copyright

1. The project will be live in your domain only after the remittance of the complete amount.
2. The client should take complete responsibility upon submitting the content (textual, graphical, or pictorial) [only for those who put forward the contents].
3. The project is mutually highlighting our talents hence it would be inscribed in our portfolio.
4. Webandcrafts has possession/ownership of the files created for the website/application until the payment delivery has been made. Once the payment is remitted, the script's complete ownership will be delivered to your concern.

11.2 Termination Terms

This Proposal/Agreement may be terminated by either Party immediately without prejudice to its accrued rights, upon the occurrence of any of the following events:

1. By either Party ("Non-Defaulting Party") where the other Party ("Defaulting Party") fails to comply with any of the terms of this Agreement, and such failure if capable of being remedied is not remedied within 30 days from the notice from the Non-Defaulting Party requiring the same to be remedied, or
2. By the Non-Defaulting Party where the Defaulting Party makes any representation or warranty pursuant to this Agreement or commits a material breach;

Copyright © Webandcrafts 2026. All Rights Reserved.

12. Why us?

Established in the year 2012. Within 12 years of operational experience, and 350+ experienced teammates, we have expanded our client presence across the globe. Well-distinguished teams across the domains of Experience Design, Technology, Digital Marketing, and Web Hosting services.

Starting as a web design company, Webandcrafts in a short time has established itself as one of the most trusted IT Solutions providers in the country.

spec-lakeshore-bepsoke-web-v3.0 | Copyright © Webandcrafts 2026. All Rights Reserved.

13. Next Step

1. Please read the contract to make sure you understand all the details involved with us working together. It’s really important to us that everything is transparent and understood from the beginning so that we lay a solid foundation for a great working relationship.
2. If you have any questions, please let us know. We’re happy to clarify any points and there may be some items that we can sort out together. We’re committed to finding the best way to work together.
3. Once you feel confident about everything and are ready to move forward, please sign the approval below and send us a signed copy.
4. Once we receive notification of your acceptance, we’ll send you the signed contract and contact you shortly to sort out the next steps and get the project rolling.
5. If you’d like to speak to us by phone, please don’t hesitate to call.

spec-lakeshore-bepsoke-web-v3.0 | Copyright © Webandcrafts 2026. All Rights Reserved.

14. Approval from the Client

Name:	Name:
Acceptance Date:	Acceptance Date:
Title:	Title:
Company:	Company:
Signature:	Signature:
_____	_____

Thanking you

Webandcrafts.

Infopark Thrissur, Kerala, India.

Copyright © Webandcrafts 2026. All Rights Reserved.

Appendix I - Recent Works from Healthcare Domain

Amrita Hospitals

Amrita, the leading healthcare provider, approached WAC for an optimised and user-friendly website to transform their digital presence. Our team designed and developed a bespoke website with high functionality and a user-centric experience to scale the efficacy of their healthcare services.

Website URL : www.amritahospitals.org

Mar Sleeva Medicity

Mar Sleeva Medicity, a leading multi-speciality hospital in Kerala, approached us to craft a responsive website with a neat layout and specular content. In keeping with their primary objective, we created a user-centric website with visually appealing designs and crisp content.

Website URL : www.marsleevamedicity.com

Skin Secrets

Skinsecrets, under the leadership of Dr. Anjana, is pioneering painless, non-surgical cosmetic skin treatments. They needed a consistent brand presence in the digital platform. With their association with Webandcrafts, we could actively radiate their brand presence through a digital glow-up to leave a lasting impression.

Website URL : www.skinsecret.co.in

Nestu Health

Nestu is destined to bring qualitative human healthcare to companion pets, with a proven record of success across the Middle East and North Africa. Webandcrafts gave life to their website, which evoked an emotional connection between humans and furry friends while also scaling the healthcare business with a unique digital paw print.

Website URL : www.nestu.health

spec-lakeshore-bepsoke-web-v3.0 | Copyright © Webandcrafts 2026. All Rights Reserved.

VCare Polyclinic

V-Care Polyclinic, established in 2014, is a professionally managed medical clinic under the patronage of Abdulrahman Ahmad Mohammad Sultan. When they approached Webandcrafts, their vision was clear: to create a website that would enhance their digital presence and establish them as a recognised healthcare brand.

Website URL : www.vcarepolyclinic.com

Vijayan Master's Ayurveda

Created a new eCommerce store for the branded organic beauty care product dealer to gain more recognition and nourish their sales channels with technical intelligence and creative goodness. The flawless finish of the technical logic gelled well with the sales perspective, fuelling their revenue.

Website URL : wwww.vijayanmastersayurveda.com

spec-lakeshore-bepsoke-web-v3.0 | Copyright © Webandcrafts 2026. All Rights Reserved.

Appendix II - Case Studies

i) IKEA - Transforming IKEA's Food E-commerce Experience
webandcrafts.com/works/ikea-foods

ii) DTALE Modern - Delivering Aesthetic Interfaces for a Digital Tale

webandcrafts.com/works/dtale

iii) Caribou Coffee - Digital Takeoff with a Complete App

webandcrafts.com/works/caribou-coffee

iv) Oxygen Digital - A Digital Revolution in Online Shopping

webandcrafts.com/works/oxygen-digital

v) Turtle Wax - User-Engaging Website to Boost Car Care Services

webandcrafts.com/works/turtlewax

vi) Lulu Hypermarket - Creating Breakthroughs in Shopping Experience

webandcrafts.com/works/lulu-hypermarket

vii) MDX University - Crafting A New Digital Theory For An Enriching Experience

webandcrafts.com/works/mdx

Other case studies can be witnessed by visiting this link here.

spec-lakeshore-bepsoke-web-v3.0 | Copyright © Webandcrafts 2026. All Rights Reserved.

Appendix III - Client References

i) Mr. Rizvi Iqubal - Digital Product Manager, IKEA (Al-Futtaim), UAE

E: rizvi.iqubal@alfuttaim.com | **P:** +971 56 671 2545

ii) Mr. Hafees Aboobakkar - Senior Webmaster & Data Lead, MDX University, UAE

E: H.Aboobakkar@mdx.ac.ae | **P:** +971 55 526 7297

iii) Mr. Bijoy Vijayaraghavan - Manager, Marketing & Communications, Swan Global, Qatar

E: bijoy@swan.qa | **P:** +974 7737 9585

iv) Mr. Midhun Subramanian - Marketing Manager, Tripgain, India

E: midhun@tripgain.com | **P:** +91 96862 01831

v) Mr. Sreejith - Manager (Software), Joy Alukkas, UAE

E: sreejith@joyalukkas.com | **P:** +971 50 458 4048

vi) Mr. Suresh Chacko - IT Director, Caribou Coffee (Alsayer Franchising), Kuwait

E: sureshc@alsayerfranchising.com | **P:** +965 9918 1699

vii) Ms. Anju Anil - Manager (Digital Marketing), Bhima Group, UAE

E: anju.anil@bhima.ae | **P:** +971 50 476 3167

viii) Mr. Hasit Kakkad - General Manager - BTC Fashion, Qatar

E: h.kakkad@btcdoha.com | **P:** +974 6655 9664

spec-lakeshore-bepsoke-web-v3.0 | Copyright © Webandcrafts 2026. All Rights Reserved.

Appendix IV - Recommended Server Configuration

Server Specifications	
Provider	Azure
Web Server	Apache
Operating System	Ubuntu 20.04
Region	Mumbai
Instance Type	D2V3 Standard
CPU	2vCPU
RAM	8 GB
Storage	50 GB SSD
No. Static IP	1
Backup	Daily (Retention 3 days)

spec-lakeshore-bepsoke-web-v3.0 | Copyright © Webandcrafts 2026. All Rights Reserved.

Appendix V - Recommended AI Addons

1. 24/7 Medical Chatbot

Handles FAQs, post-discharge care queries and general questions — reducing call center load.

2. Doctor/Specialist Finder

AI recommends the right specialist based on symptoms, insurance, location, and availability, not just a static directory.

3. Smart Search

Semantic search across doctors, departments, conditions, and procedures — understanding intent, not just keywords.

4. Medical Report Summarizer

Patients upload lab reports or discharge summaries and get plain-language explanations instead of medical jargon.

5. Feedback Collection using AI Agent

An AI voice agent will automatically initiate a call to the patient after discharge to collect their feedback. The QA team can then access and review the reports through the backend system.

**All the above mentioned AI features will be dependent on LLM models such as Gemini, and will incur usage-based charges calculated based on token consumption.*

spec-lakeshore-bepsoke-web-v3.0 | Copyright © Webandcrafts 2026. All Rights Reserved.
